

Jira Agile Backlog and Sprint Simulation

Airport Lost Luggage and Tracking Portal

Prepared by	Aditya Patil
Jira space	Airport Lost Luggage and Tracking Portal ALLTP
Submission date	4 September 2026

Work Completed

The Jira space contains three epics and five user stories based on the airport lost-luggage scenario. Each story has a parent epic, a High, Medium, or Low priority, and a Fibonacci story-point estimate. Two one-week sprints were started, progressed through To Do, In Progress, and Done, and completed in Jira.

Item	Planned scope	Result
Epics	3	Claim registration, tracking and recovery, compensation and resolution
User stories	5	All linked to epics with descriptions and acceptance criteria
Sprint 1	18 points	3 of 3 stories completed
Sprint 2	11 points	2 of 2 stories completed

Epic Structure

Key	Epic	Purpose
ALLTP-1	Claim Registration and Validation	Register claims using bag tag and itinerary details and reject invalid input.
ALLTP-2	Tracking and Recovery	Match claims to scan logs, display scan history, and notify passengers.
ALLTP-3	Compensation and Resolution	Evaluate eligibility, record approved compensation, and resolve cases.

Prioritized Product Backlog

The five user stories are ordered across the two sprints according to user impact and implementation sequence. Story points estimate relative effort and uncertainty rather than elapsed hours.

Key	Story	Epic	Priority	Points	Sprint
ALLTP-4	Submit a lost baggage claim	Claim Registration and Validation	High	5	Sprint 1
ALLTP-5	Match claims with unlocated baggage scans	Tracking and Recovery	High	8	Sprint 1
ALLTP-6	View the complete baggage scan timeline	Tracking and Recovery	Medium	5	Sprint 1
ALLTP-7	Receive baggage recovery notifications	Tracking and Recovery	Medium	3	Sprint 2
ALLTP-8	Process eligible passenger compensation	Compensation and Resolution	Low	8	Sprint 2

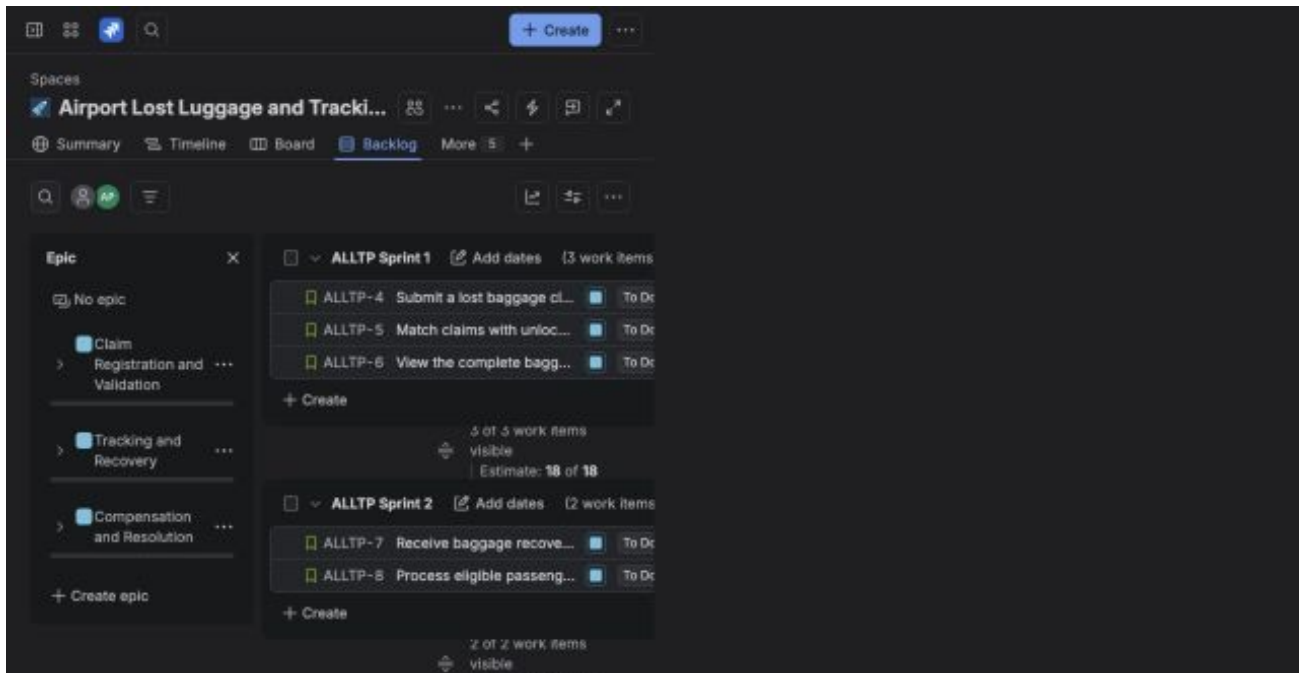


Figure 1 Jira backlog with the epic panel, both planned sprints, user stories, priorities, and story-point totals

Sprint Execution

Both sprints were planned for one week and executed sequentially during the lab simulation. Each story was moved through To Do, In Progress, and Done before its sprint was completed.

Sprint	Planned dates	Points	Stories	Done	Goal
ALLTP Sprint 1	4 Sep to 11 Sep 2026	18	3	3	Claim intake, scan matching, and passenger timeline
ALLTP Sprint 2	4 Sep to 11 Sep 2026	11	2	2	Recovery notifications and compensation decision

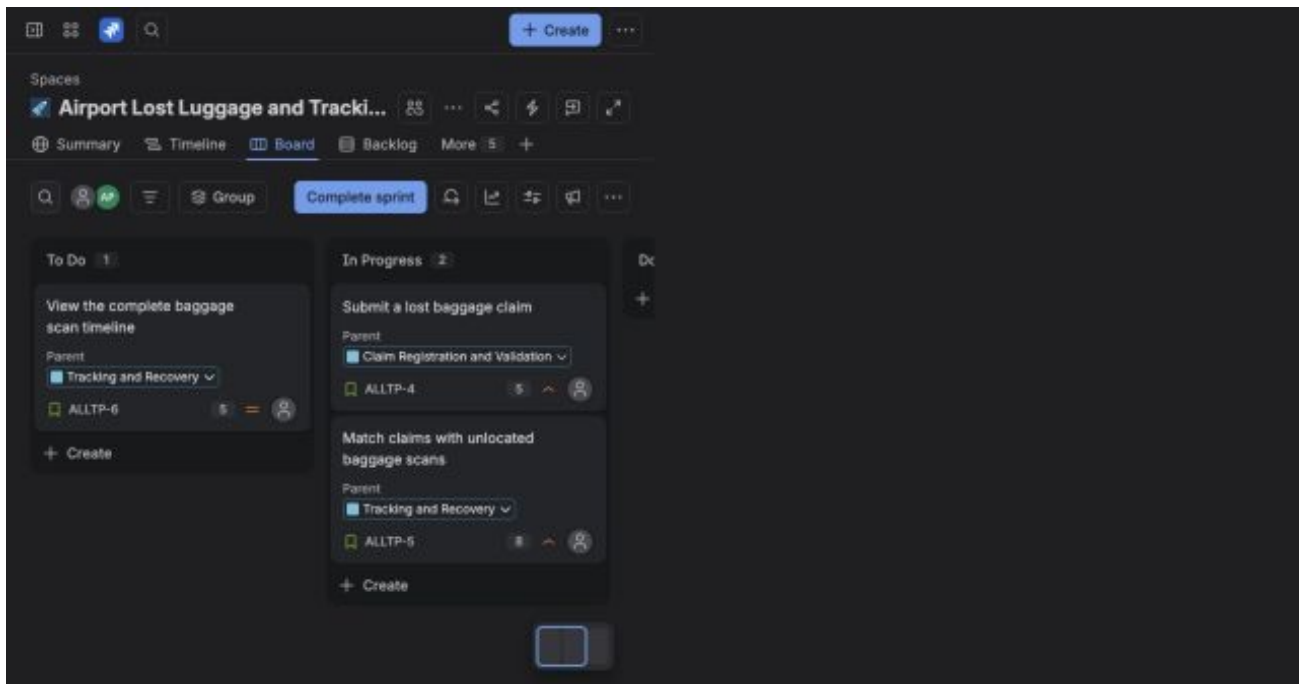


Figure 2 Active Sprint 1 with one story in To Do and two stories in In Progress

Second Sprint Progress

Sprint 2 began after Sprint 1 was completed. The board below records the second simulation step, with one story in progress and one story still in To Do.

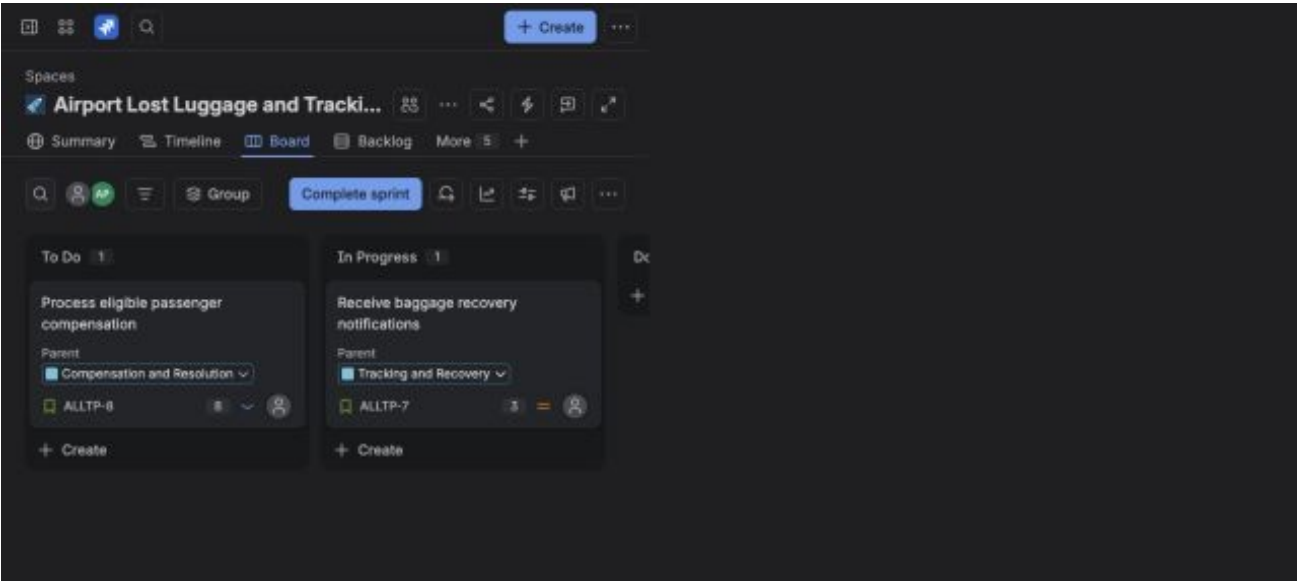


Figure 3 Active Sprint 2 with notification work in progress and compensation work in To Do

After this screenshot, both Sprint 2 stories were moved to Done and the sprint was completed. Jira recorded all 11 planned story points as completed.

Sprint Burndown Chart

Jira generated the Sprint 2 burndown report using story points. The sprint contained 11 points and no scope was added after the sprint started.

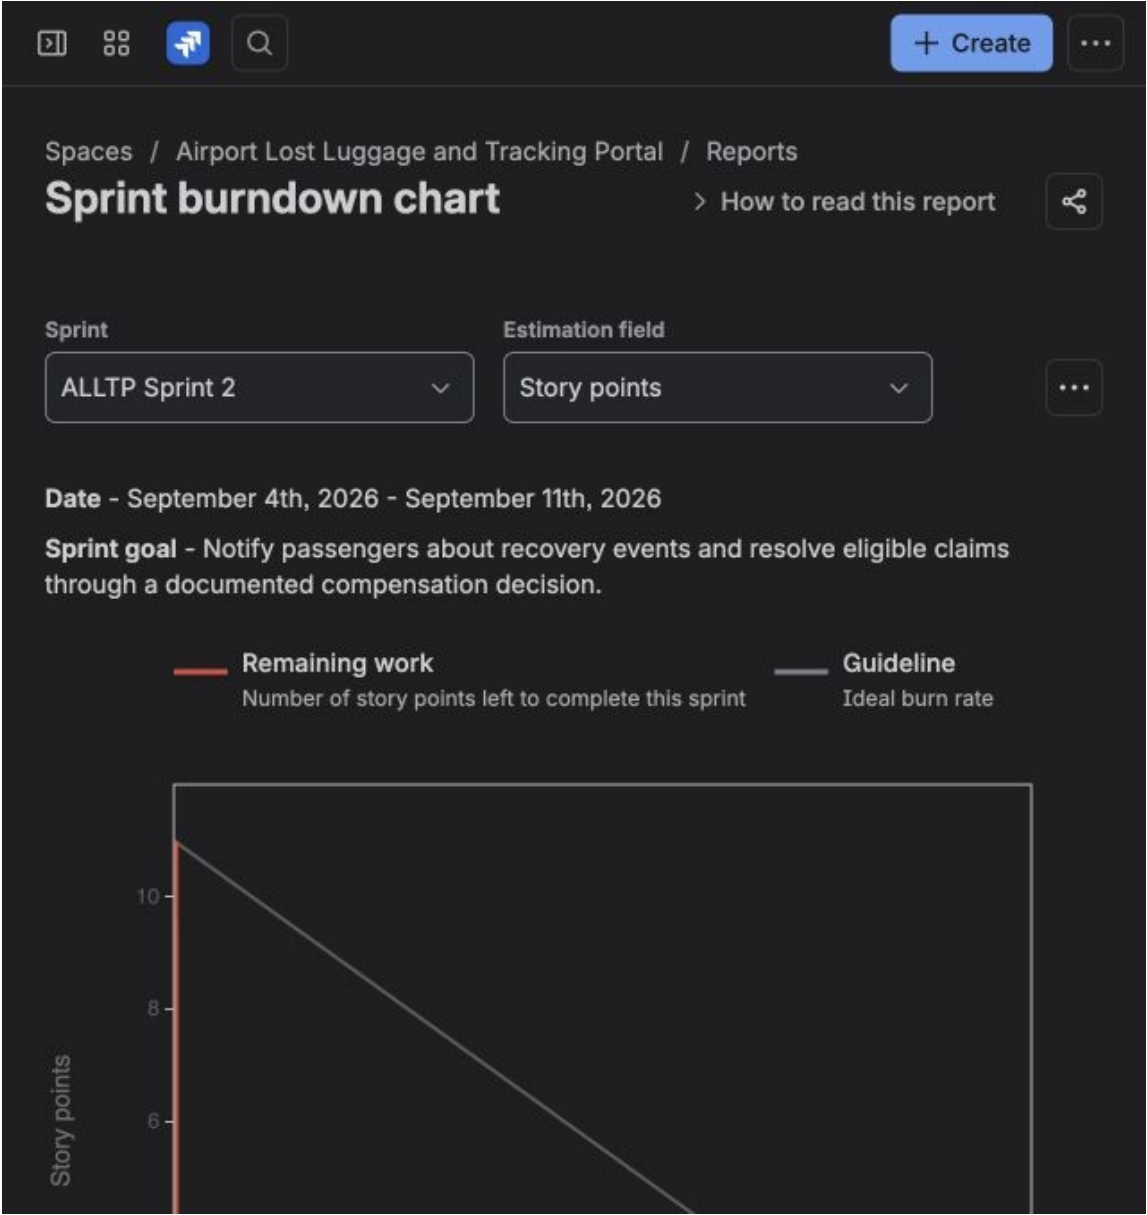


Figure 4 Sprint 2 report settings, planned dates, sprint goal, and chart legend

Burndown Result

The remaining-work line falls from 11 story points to zero on the start date because the lab simulated all status changes in one session. The ideal guideline continues to the planned end date.

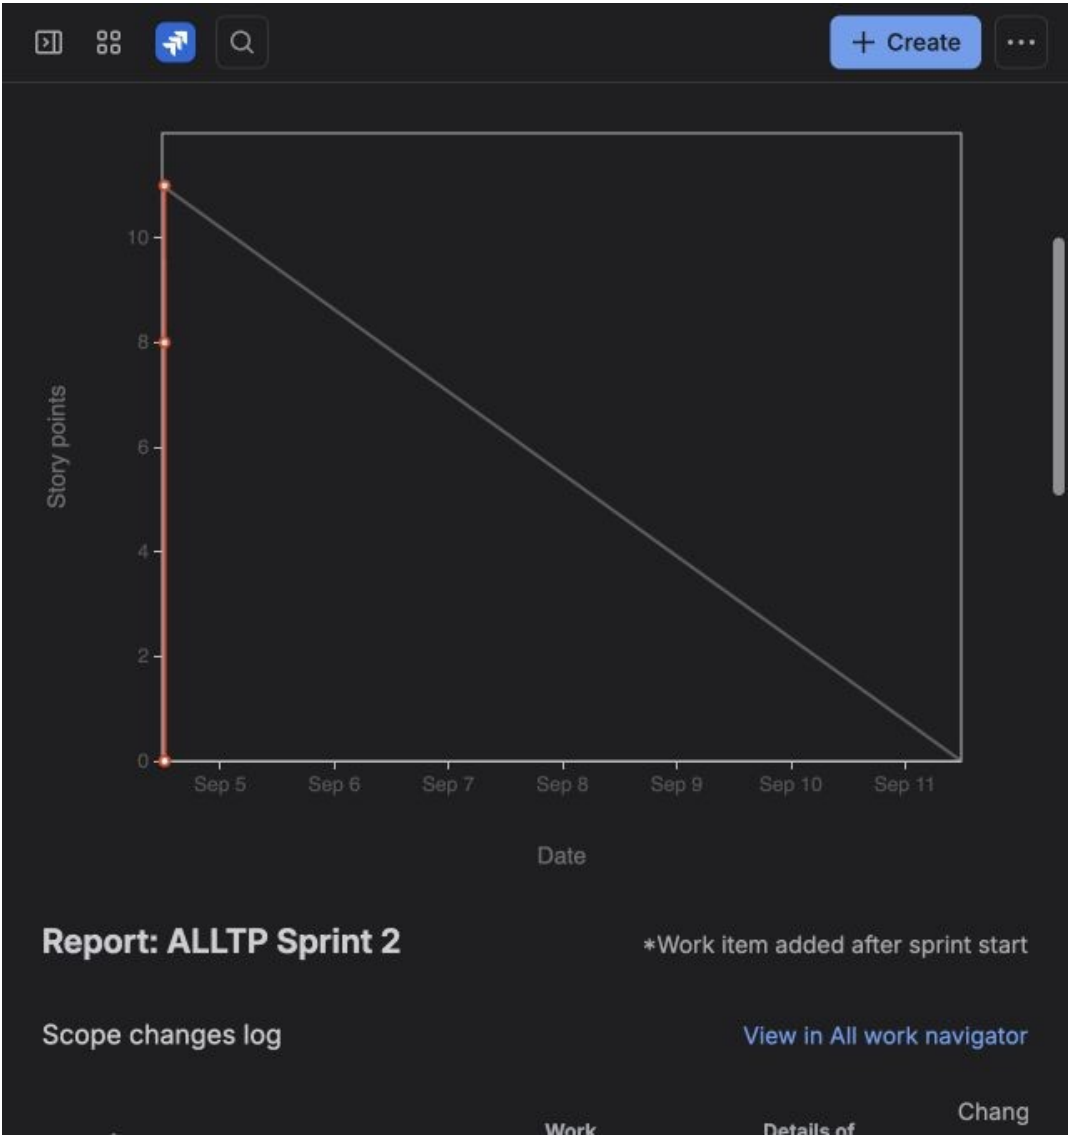


Figure 5 Sprint 2 burndown graph showing all 11 points completed on 4 September 2026

Reflection Questions

1 Did the estimations reflect the actual effort

The estimates reflect relative complexity, but this simulation did not include real implementation time. Scan matching and compensation received 8 points because they involve integrations, rules, and greater uncertainty. Notifications received 3 points, while claim submission and timeline display received 5 points each. A real sprint would be needed to compare those estimates with actual delivery effort.

2 Was the backlog well prioritized

Yes. Sprint 1 placed the High-priority claim submission and baggage-matching stories before the Medium-priority timeline story. Sprint 2 then handled notifications and compensation. Compensation was marked Low relative to immediate recovery work even though its 8-point estimate shows that it is complex. Priority and effort were treated as separate decisions.

3 How did the simulated sprint align with the plan

The simulation completed all planned scope: 18 points across three Sprint 1 stories and 11 points across two Sprint 2 stories. Every story moved through To Do, In Progress, and Done. Completion occurred much earlier than the one-week time boxes because the exercise simulated workflow rather than software development.

4 What did the burndown chart show about team capacity

The Sprint 2 chart shows a vertical drop from 11 points to zero on 4 September, well below the ideal guideline. It confirms that the planned work was marked complete and that no scope was added after the sprint started. It does not establish sustainable team capacity because all work was updated in one session. The 11-point result should be treated as an illustrative velocity, not a forecast for a real team.

Submission Summary

The Jira space is ready for instructor review. It contains the completed epic hierarchy, user stories with acceptance criteria, visible priorities and Fibonacci estimates, two completed sprints, and the Sprint 2 burndown report.
